










OWNER:  شرکت سست و سویی توهم ایرانیان (سهامی خاص)	BUSHEHR PETROCHEMICAL COMPANY MEG PLANT						EPC CONTRACTOR:  Chagalesh-Enerechimi-Steam Joint Venture BUPC-MEG PLANT PROJECT		
	BI-WEEKLY PROGRESS REPORT							 Netherlands	
MC :   شرکت سست و سویی توهم ایرانیان (سهامی خاص)	Project	Area	Phase	Unit	Dis.	Doc.	Seq.	Contract No : 52-98/445	
Owner Document Number: 17811-74	BU	20	VD	303	PC	MRP	0004	Rev.:	Page
								06	1 of 12

BI-WEEKLY PROGRESS REPORT

06	14/01/2022	Issue For Review			JR	KP	PW	
00	14/09/2021	Issue For Review			JR	KP	PW	
Rev.	Date	Purpose of Issue			Prepared	Checked	Approved	AC Code
							Class: 1	Phase: P

 <p>شرکت سست، موی آبر ایران (سهامی خاص)</p>	BUSHEHR PETROCHEMICAL COMPANY MEG PLANT Bi-Weekly Progress Report	  <p>Chagaleh-Enerchimi-Steam JOINT VENTURE BUPC-MEG PLANT PROJECT</p>						
	<table border="1" style="width: 100%;"> <tr> <td style="width: 30%;">DOCUMENT No.</td> <td style="text-align: center;">17811-74</td> </tr> <tr> <td>'DOCUMENT TITLE</td> <td style="text-align: center;">Progress Report</td> </tr> </table>	DOCUMENT No.	17811-74	'DOCUMENT TITLE	Progress Report	<table border="1" style="width: 100%;"> <tr> <td style="text-align: right;">Doc. Class: 2</td> </tr> <tr> <td style="text-align: right;">Page 1 of 6</td> </tr> </table>	Doc. Class: 2	Page 1 of 6
DOCUMENT No.	17811-74							
'DOCUMENT TITLE	Progress Report							
Doc. Class: 2								
Page 1 of 6								

<p>Bi-Weekly Progress Report</p>
PO (Package) Description: Reciprocating compressor
PO No: 52-98/445
Vendor Name : Airpack Netherlands B.V.
Report No. : 0019
Cut-Off date: January 13th, 2022
Plan Progress : 29%
Actual Progress : 29%

06	13-1-2022	JR	KP	JR	JR	Issue For Review
REV.	ISSUE DATE	PREPARED	CHECKED	Project Manager	APPROVED	PURPOSE OF ISSUE



Progress Report Format											
Req. No.:					Item No. ALL ITEMS						
P/O No.: MEG20-PO-BP303-021					Description : reciprocating compressor						
Delivery Condition:				Delivery Date	dd	mm	yy		dd	mm	yy
EXW	<input checked="" type="checkbox"/>	CFR	<input type="checkbox"/>	Contractual				as of			
FOB	<input type="checkbox"/>	DDU	<input type="checkbox"/>	Last Promised	1	7	22	as of	15	12	21
Location: Assaluyeh				Present Estimate				as of			
This report covers Progress for the period of					15	12	21	-	13	1	22
					start:			End:			
Major activities which have been done in this Period:											
Pulsation ongoing results air compressor in draft known. Nitrogen pulsation study is in final stage											
Nitrogen Compressor will be redesigned due to the fact that the pulsation study concluded more capacity was needed.											
Airpack is waiting on the Nitrogen compressor P&ID											
Compressor delivery sheduled for end January 2022											
Major Activities for Next Period:											
Pulsation dampers ordering will be January											
Attachment:											
X Fabrication schedule					<input type="checkbox"/> Sub-Order Status Report						
X Document Status Report					<input type="checkbox"/> Other Document						
Remaining Open Items to be settled with CONTRACTOR.											
No											
Problem: (relating Letter/Fax No.					Dated						
Problems which may affect on quality of the Product or delivery schedule.											
Explanation of problem: (informed to CONTRACTOR by Letter/Fax No.											
Dated											
Discharge pressure of the compressor (as per CRS of P&ID)											
Document turn around longer then 10 workingdays											
Return time CRS to long											
Procedure returning documents gives confusion and it's easy to mis documentation.											
Client asking to go back to a previous revision number is not possible, due to ISO regulations											
Wrong revions are send back											
Impact to Quality of product and/or fabrication/delivery schedule.											
Status of Countermeasure and schedule.											
Required urgent Information or returning of approved documents by CONTRACTOR.											
yes											
Customer Piping ISOMETRICS required to finalize pulsation study											
Others											
Jeroen Rust Commercial Project Manager											



شرکت سست و سوهی آهوا ایران
(سهامی خاص)



گروه صنعتی پتروشیمی

**BUSHEHR PETROCHEMICAL
COMPANY
MEG PLANT**



Chagalesh-Enerchimi-Steam
Joint Venture
BUPC-MEG PLANT PROJECT

DOCUMENT TITLE

DOCUMENT No. 17811-74

Doc. Class: 3

Progress Report

Page 3 of 6

ACTIVITY	WEIGHT FACTOR	SCHEDULE PLAN		ACTUAL STATUS			
		START	FINISH	START DATE	FINISH DATE	PROGRESS	
						Plan	Actual
ENGINEERING	15%	30-Sep-21	13-Oct-21	30-Sep-20		35%	35%
PROCUREMENT	25%	1-Feb-21	29-Dec-21	26-Jun-21		57%	57%
FABRICATION	45%	1-Oct-21	14-Apr-22			20%	20%
INSPECTION	5%	7-Mar-22	6-Jul-22			5%	5%
SHIPMENT	5%	22-Jul-22	22-Jul-22			0%	0%
FINAL DATA BOOK	5%	7-Mar-22	22-Jul-22			0%	0%
OVERAL	100%					29%	29%



Area of Concern

Relation between contractor, end- user and supplier under pressure

Technical comments are difficult to implement on the size the compressors

World wide supply chain is disrupted due to the Covid19 Pandemic. This leads to long delivery times for motors (24 weeks) electrical components, PLC material, raw material and etc.

Wrong revisions sent back. Airpack sent revision 3 and received back comments on rev 2. Document will be rejected. Comments can only be given once.



Executive Summary

Engineering


Continue with calculations for the pulsation demper

Continue with updating engineering documents

Procurement

Avalibility and delivery time of PLC, electrical components, valves and raw material is risc.
Delivery times become extreem longer.

Fabrication, Test, Shipment

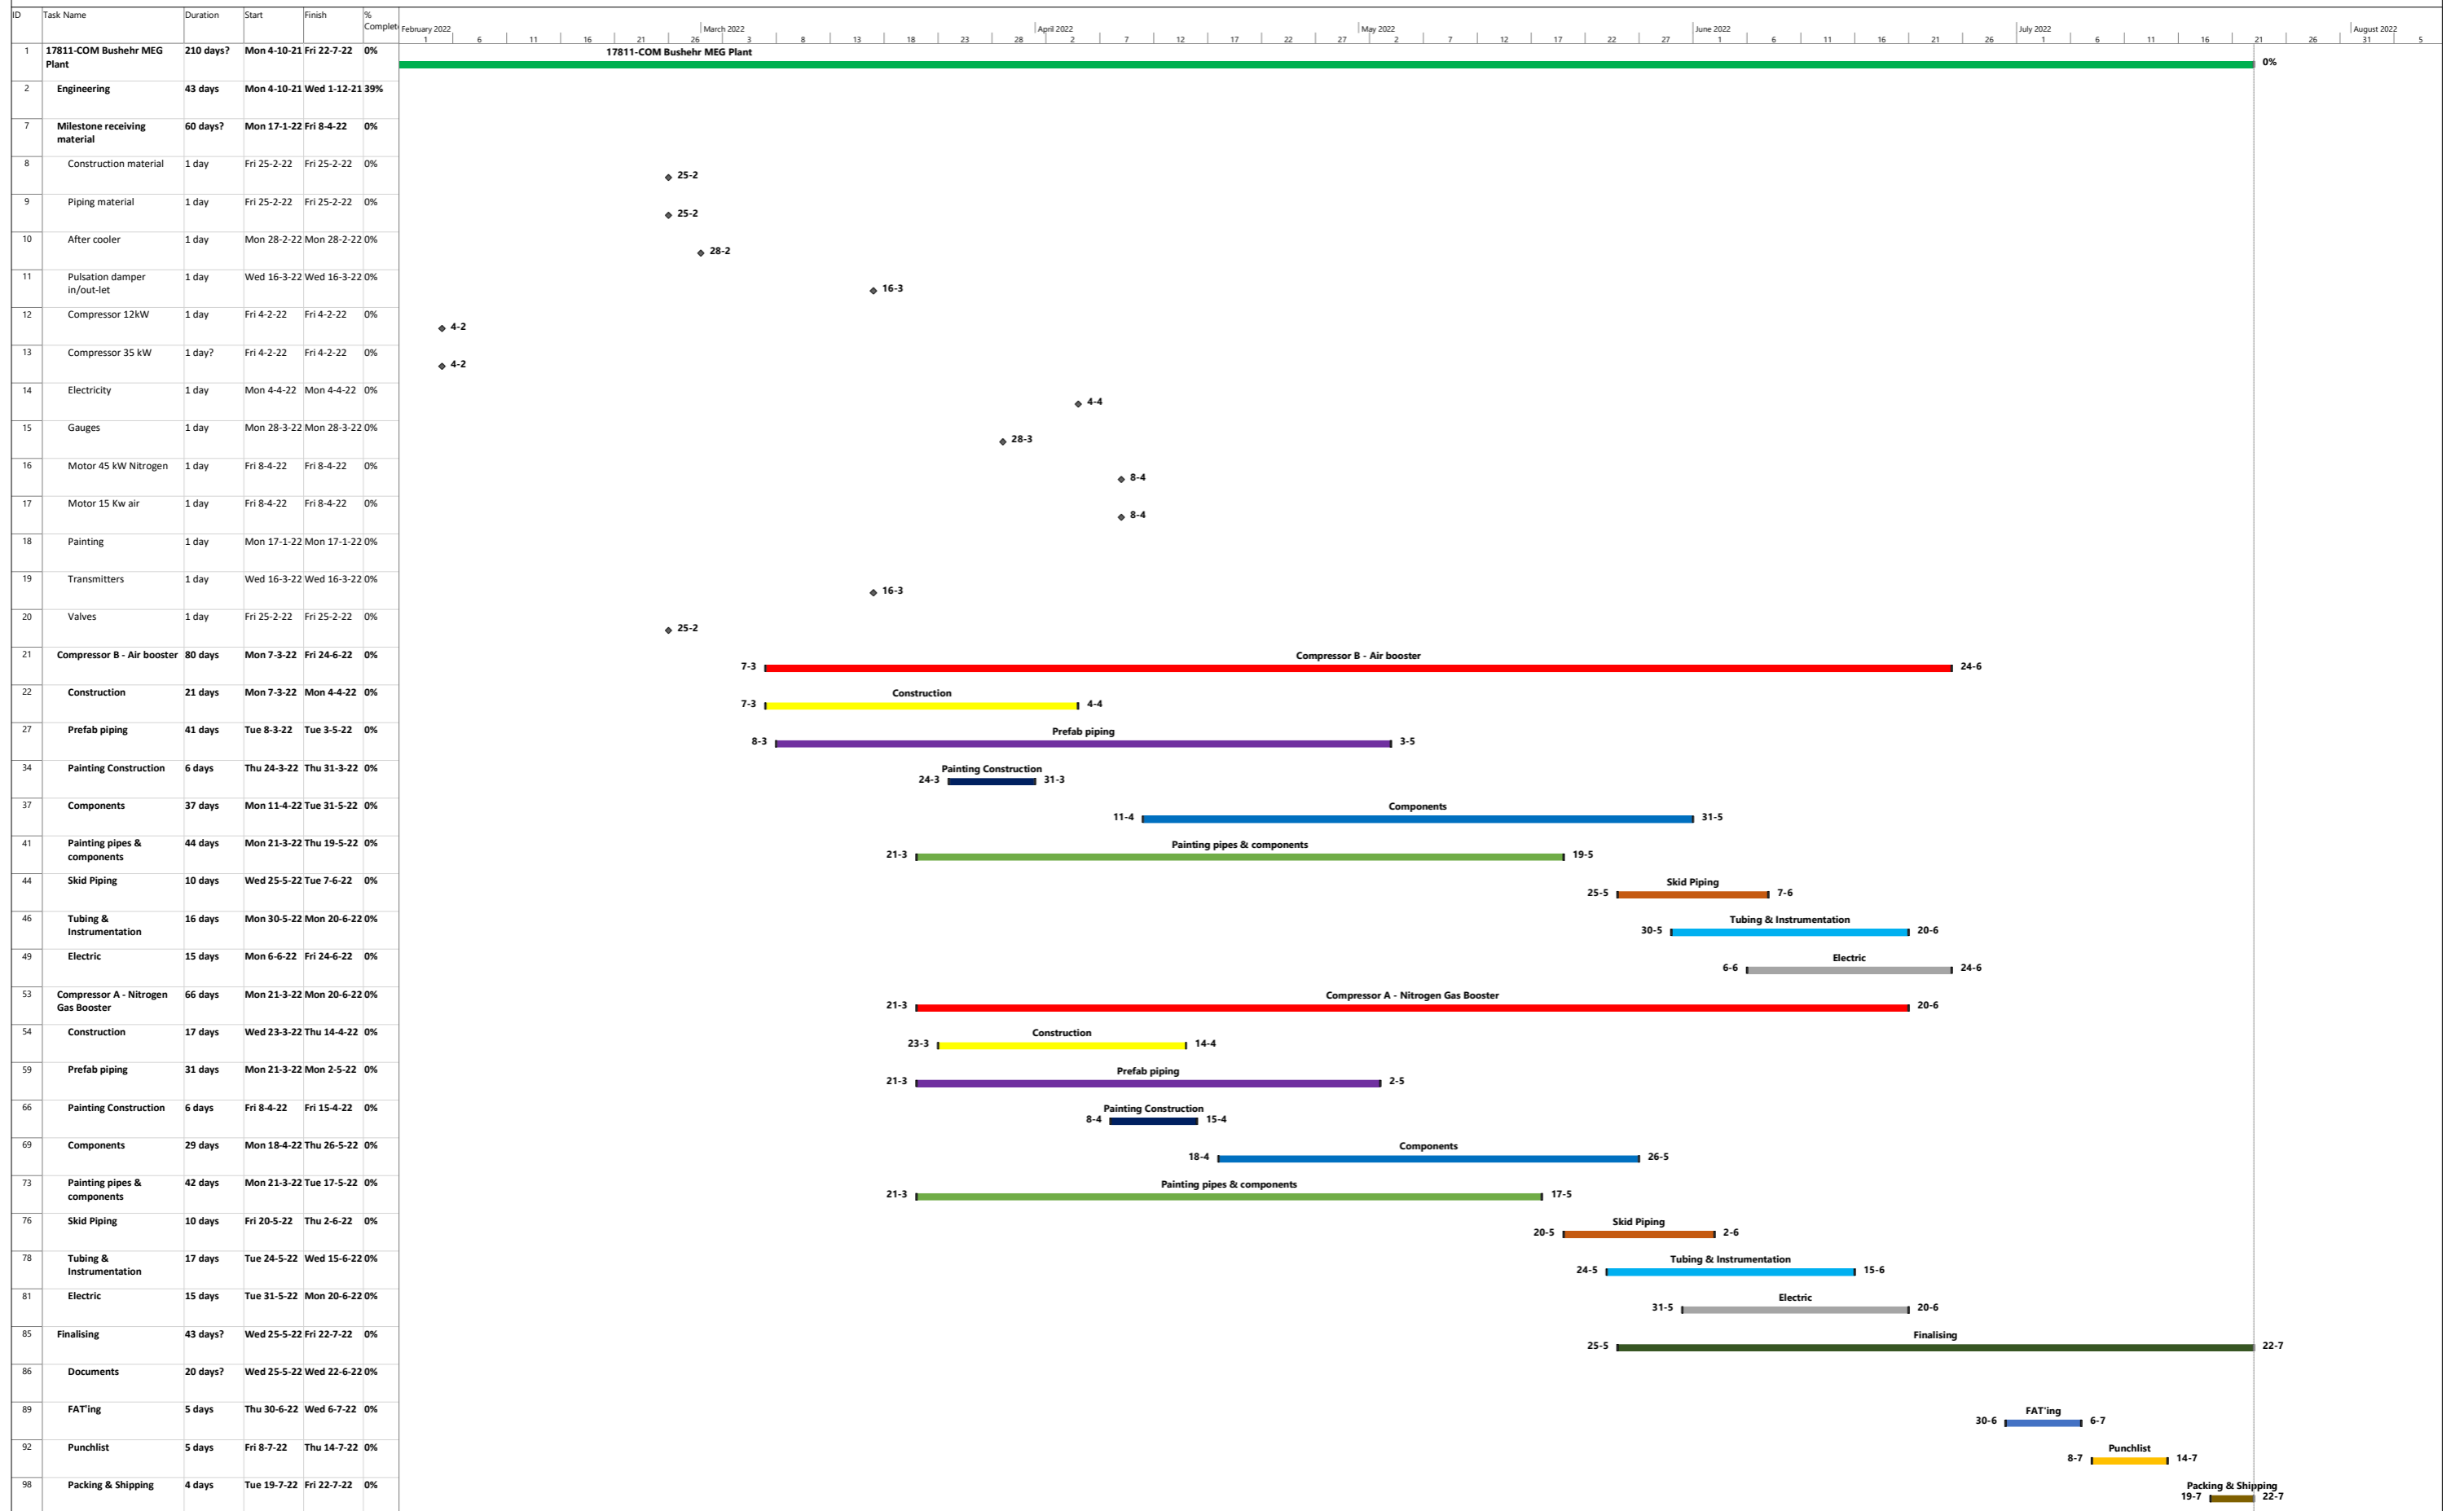

VENDOR DOCUMENT SCHEDULE



Project:	Bushehr MEG Plant Project			
Purchase order:	MEG20-PO-BP303-021			
Airpack reference:	17811-COM			
Project manager:	Kevin Pool/Jeroen Rust			
Document turn around time:	: 10 workdays (5 workdays is 1 week!)			

IFC IFA IFI AFC AB	AP AN CM RE: Rejected NC
--------------------------------	--------------------------------------

Airpack document number	Revision number (00 - 09)	Contractor / Customer Document number	Description	Usage	Document issue date		Document return date		Approval Code	Days of delay (5 days = 1 working week)	Transm. nr.
					Planned date	Actual date	Planned date	Actual date			
17811-01	05	BU-20-VD-303-DC-DCI-0001	VENDOR PRINT INDEX & SCHEDULE (VPIS) FOR RECIPROCATING COMPRESSORS & NITROGEN GAS BOOSTER	IFA	21-01-22					#VALUE!	
17811-03A	01	BU-20-VD-303-PR-DWG-0013	P&ID FOR NITROGEN GAS BOOSTER INCL. CRS	IFA	05-11-21	04-11-21	18-11-21			42 days	0045
17811-03B	04	BU-20-VD-303-PR-DWG-0066	P&ID FOR EMERGENCY INSTRUMENT AIR COMPRESSOR INCL. CRS	AFC	18-01-22	07-01-22	21-01-22			-6 days	0079
17811-04A	05	BU-20-VD-303-ME-DWG-0023	GENERAL ARRANGEMENT DRAWING FOR NITROGEN GAS BOOSTER INCL. CRS	AFC	19-01-22					#VALUE!	
17811-04B	07	BU-20-VD-303-ME-DWG-0076	GENERAL ARRANGEMENT DRAWING FOR EMERGENCY INSTRUMENT AIR COMPRESSOR	IFA	19-01-22					-4 days	0055
17811-05A	03	BU-20-VD-303-IN-DIG-0043	UCP/LCP/JB WIRING DIAGRAM FOR NITROGEN GAS BOOSTER	IFA	31-01-22					-12 days	
17811-05B	03	BU-20-VD-303-IN-DIG-0093	UCP/LCP/JB WIRING DIAGRAM FOR EMERGENCY INSTRUMENT AIR COMPRESSOR INCL. CRS	IFA	31-01-22					-12 days	
17811-06A	02	BU-20-VD-303-IN-LST-0034	I/O LIST FOR NITROGEN GAS BOOSTER INCL. CRS	AFC	27-12-21	06-01-22	20-01-22			-5 days	0075
17811-06B	02	BU-20-VD-303-IN-LST-0084	I/O LIST FOR EMERGENCY INSTRUMENT AIR COMPRESSOR INCL. CRS	AFC	27-12-21	06-01-22	20-01-22			-5 days	0075
17811-07A	02	BU-20-VD-303-IN-DWG-0039	UCP/LCP/JB GENERAL ARRANGEMENT DRAWING & TERMINAL DETAILS FOR NITROGEN GAS BOOSTER INCL. BOM INCL. CRS	IFA	22-11-21	14-12-21	28-12-21			14 days	0068
17811-07B	02	BU-20-VD-303-IN-DWG-0089	UCP/LCP/JB GENERAL ARRANGEMENT DRAWING & TERMINAL DETAILS FOR EMERGENCY INSTRUMENT AIR COMPRESSOR INCL. BOM INCL. CRS	IFA	22-11-21	14-12-21	28-12-21			14 days	0068
17811-08	05	BU-20-VD-303-QC-ITP-0005	INSPECTION & TEST PLAN (ITP)	AFC	18-01-22	06-01-22	20-01-22			-5 days	0076
17811-09A	00	BU-20-VD-303-PR-LST-0014	UTILITY CONSUMPTION LIST FOR NITROGEN GAS BOOSTER	IFA	25-02-22					#VALUE!	
17811-09B	00	BU-20-VD-303-PR-LST-0067	UTILITY CONSUMPTION LIST FOR EMERGENCY INSTRUMENT AIR COMPRESSOR	IFA	25-02-22					#VALUE!	
17811-10A	04	BU-20-VD-303-EL-DSH-0051	COMPRESSOR MOTOR DATA SHEET FOR NITROGEN GAS BOOSTER	AFC	27-12-21	06-01-22	20-01-22			-5 days	0077
17811-10B	04	BU-20-VD-303-EL-DSH-0099	COMPRESSOR MOTOR DATA SHEET FOR EMERGENCY INSTRUMENT AIR COMPRESSOR	AFC	27-12-21	06-01-22	20-01-22			-5 days	0077
17811-11A	03	BU-20-VD-303-ME-DSH-0022	MECHANICAL DATA SHEET FOR NITROGEN GAS BOOSTER INCL. CRS	AFC	31-01-22					#VALUE!	
17811-11B	02	BU-20-VD-303-ME-DSH-0017	AFTER COOLER MECHANICAL DATA SHEET FOR NITROGEN GAS BOOSTER	IFA	31-01-22					#VALUE!	
17811-11C	01	BU-20-VD-303-ME-DSH-0027	PULSATION DAMPER MECHANICAL DATA SHEET FOR NITROGEN GAS BOOSTER	IFA	31-12-21					#VALUE!	
17811-11D	02	BU-20-VD-303-EL-DWG-0021	LUBE OIL SYSTEM HEATER DATA SHEET AND DRAWING FOR NITROGEN GAS BOOSTER	IFA	18-01-22					#VALUE!	
17811-11E	03	BU-20-VD-303-ME-DSH-0019	MAIN OIL PUMP MECHANICAL DATA SHEET FOR NITROGEN GAS BOOSTER	AB	after FAT					#VALUE!	
17811-11F	03	BU-20-VD-303-ME-DSH-0020	LUBE OIL SYSTEM FILTER MECHANICAL DATA SHEET FOR NITROGEN GAS BOOSTER	AB	after FAT					#VALUE!	
17811-11G	03	BU-20-VD-303-ME-DSH-0075	MECHANICAL DATA SHEET FOR EMERGENCY INSTRUMENT AIR COMPRESSOR INCL. CRS	AFC	18-01-22					#VALUE!	
17811-11H	01	BU-20-VD-303-ME-DSH-0070	AFTER COOLER MECHANICAL DATA SHEET FOR EMERGENCY INSTRUMENT AIR COMPRESSOR	IFA	19-01-22					#VALUE!	
17811-11I	01	BU-20-VD-303-ME-DSH-0028	PULSATION DAMPER MECHANICAL DATA SHEET FOR EMERGENCY INSTRUMENT AIR COMPRESSOR	IFA	19-01-22					#VALUE!	
17811-11J	02	BU-20-VD-303-EL-DWG-0074	LUBE OIL SYSTEM HEATER DATA SHEET AND DRAWING FOR EMERGENCY INSTRUMENT AIR COMPRESSOR	IFA	04-01-22	07-01-22	21-01-22			-6 days	0078
17811-11K	03	BU-20-VD-303-ME-DSH-0072	MAIN OIL PUMP MECHANICAL DATA SHEET FOR EMERGENCY INSTRUMENT AIR COMPRESSOR	AB	after FAT					#VALUE!	

17811-11L	03	BU-20-VD-303-ME-DSH-0073	LUBE OIL SYSTEM FILTER MECHANICAL DATA SHEET FOR EMERGENCY INSTRUMENT AIR COMPRESSOR	AB	after FAT				#VALUE!	
17811-12A	04	BU-20-VD-303-IN-DSH-0040	INSTRUMENT DATA SHEET FOR NITROGEN GAS BOOSTER INCL. CRS	IFA	27-12-21	05-01-22	19-01-22		-4 days	0074
17811-12B	04	BU-20-VD-303-IN-DSH-0090	INSTRUMENT DATA SHEET FOR EMERGENCY INSTRUMENT AIR COMPRESSOR INCL. CRS	IFA	27-12-21	05-01-22	19-01-22		-4 days	0074
17811-13	00	BU-20-VD-303-ME-LST-0055	Commissioning and start-up spare parts list	IFI	15-02-22				49 days	
17811-14	01	BU-20-VD-303-QC-PRC-0009	Compressor FAT test procedure	IFA	28-01-22				49 days	
17811-15	02	BU-20-VD-303-QC-PRC-0007	NDE procedure incl. CRS	IFA	31-01-22				#VALUE!	
17811-16	00	BU-20-VD-303-ME-DWG-0029	ALL EQUIPMENT NAME PLATE DRAWING	IFA	15-02-22				#VALUE!	
17811-18	02	BU-20-VD-303-PI-DCR-0010	Surface preparation & painting procedure	CRS	22-11-21	09-11-21	12-11-21		46 days	0047
17811-18	03	BU-20-VD-303-PI-DCR-0010	Surface preparation & painting procedure	AFC	22-11-21				#VALUE!	
17811-19	00	BU-20-VD-303-DC-INX-0061	FINAL DATA BOOK INDEX FOR RECIPROCATING COMPRESSOR & NITROGEN GAS BOOSTER	IFA	31-01-22				#VALUE!	
17811-20	00	BU-20-VD-303-ME-MNL-0012	Installation, operation & maintenance manual	IFA	after FAT				#VALUE!	
17811-21A	03	BU-20-VD-303-PR-DPH-0046	CONTROL PHILOSOPHY FOR NITROGEN GAS BOOSTER INCL. CRS	AFC	24-01-22				#VALUE!	
17811-22	00	BU-20-VD-303-PE-PRC-0008	Packing, marking shipping & preservation procedure	IFA	15-02-22				#VALUE!	
17811-23A	01	BU-20-VD-303-ME-DWG-0018	AFTER COOLER DETAIL DRAWING FOR NITROGEN GAS BOOSTER	IFA	15-02-22				#VALUE!	
17811-23B	01	BU-20-VD-303-ME-DWG-0071	AFTER COOLER DETAIL DRAWING FOR EMERGENCY INSTRUMENT AIR COMPRESSOR	IFA	15-02-22				#VALUE!	
17811-23C	00	BU-20-VD-303-ME-DWG-0079	PULSATION DAMPER DETAIL DRAWING FOR NITROGEN GAS BOOSTER	IFA	15-02-22				-23 days	
17811-23D	00	BU-20-VD-303-ME-DWG-0080	PULSATION DAMPER DETAIL DRAWING FOR EMERGENCY INSTRUMENT AIR COMPRESSOR	IFA	15-02-22				-23 days	
17811-24A	00	BU-20-VD-303-ME-CAL-0016	AFTER COOLER MECHANICAL STRENGTH CALCULATION FOR NITROGEN GAS BOOSTER	IFI	31-01-22				-12 days	
17811-24B	00	BU-20-VD-303-ME-CAL-0069	AFTER COOLER MECHANICAL STRENGTH CALCULATION FOR EMERGENCY INSTRUMENT AIR COMPRESSOR	IFI	31-01-22				-12 days	
17811-24C	00	BU-20-VD-303-ME-CAL-0026	PULSATION DAMPER MECHANICAL STRENGTH CALCULATION FOR NITROGEN GAS BOOSTER	IFI	31-01-22				-12 days	
17811-24D	00	BU-20-VD-303-ME-CAL-0078	PULSATION DAMPER MECHANICAL STRENGTH CALCULATION FOR EMERGENCY INSTRUMENT AIR COMPRESSOR	IFI	31-01-22				-12 days	
17811-27A	03	BU-20-VD-303-PR-LST-0042	CAUSE & EFFECT CHART LIST FOR NITROGEN GAS BOOSTER INCL. CRS	AFC	31-01-22				#VALUE!	
17811-30A	01	BU-20-VD-303-IN-DIG-0036	LOOP DIAGRAM FOR NITROGEN GAS BOOSTER	IFA	17-02-22				#VALUE!	
17811-30B	01	BU-20-VD-303-IN-DIG-0086	LOOP DIAGRAM FOR EMERGENCY INSTRUMENT AIR COMPRESSOR	IFA	17-02-22				#VALUE!	
17811-32A	02	BU-20-VD-303-IN-DIG-0035	LOGIC DIAGRAMS-PROGRAM OF UCP - COMPRESSOR SHUTDOWN LOGIC DRAWING FOR NITROGEN GAS BOOSTER INCL. CRS	AFC	04-01-22	06-01-22	20-01-22		-5 days	0076
17811-32B	02	BU-20-VD-303-IN-DIG-0085	LOGIC DIAGRAMS-PROGRAM OF UCP - COMPRESSOR SHUTDOWN LOGIC DRAWING FOR EMERGENCY INSTRUMENT AIR COMPRESSOR INCL. CRS	AFC	04-01-22	06-01-22	20-01-22		-5 days	0076
17811-36A	03	BU-20-VD-303-IN-LST-0037	TRIP & ALARM SETPOINT LIST FOR NITROGEN GAS BOOSTER INCL. CRS	AFC	20-12-21	06-01-22	20-01-22		-5 days	0075
17811-36B	01	BU-20-VD-303-IN-LST-0087	TRIP & ALARM SETPOINT LIST FOR EMERGENCY INSTRUMENT AIR COMPRESSOR INCL. CRS	IFA	27-10-21	04-11-21	18-11-21		42 days	0046
17811-38A	02	BU-20-VD-303-IN-DWG-0033	INSTRUMENT HOOK UP DRAWING FOR NITROGEN GAS BOOSTER INCL. CRS	IFA	31-01-22				#VALUE!	
17811-38B	01	BU-20-VD-303-IN-DWG-0103	INSTRUMENT HOOK UP DRAWING FOR EMERGENCY INSTRUMENT AIR COMPRESSOR	IFA	31-01-22				#VALUE!	
17811-39A	02	BU-20-VD-303-EL-DWG-0053	COMPRESSOR MOTOR OUTLINE DRAWING & TERMINAL BOX WIRING DIAGRAM FOR NITROGEN GAS BOOSTER INCL. CRS	IFA	18-01-22	06-01-22	20-01-22		-5 days	0077
17811-39B	02	BU-20-VD-303-EL-DWG-0101	COMPRESSOR MOTOR OUTLINE DRAWING & TERMINAL BOX WIRING DIAGRAM FOR EMERGENCY INSTRUMENT AIR COMPRESSOR INCL. CRS	IFA	18-01-22	06-01-22	20-01-22		-5 days	0077
17811-42	00	BU-20-VD-303-ME-LST-0054	Two years spare parts list	IFI	15-06-22				-109 days	
17811-43	02	BU-20-VD-303-PE-LST-0002	Sub vendor list incl. CRS	IFA	15-11-21	16-11-21	30-11-21		34 days	0051
17811-44B	03	BU-20-VD-303-ME-DSH-0082	DATA SHEET & DRAWINGS FOR STRAINERS FOR EMERGENCY INSTRUMENT AIR COMPRESSOR	AFC	15-11-21	14-12-21	28-12-21		14 days	0068
17811-45A	03	BU-20-VD-303-IN-DSH-0041	CALCULATION & DATA SHEET OF CONTROL VALVES / ON-OFF VALVES FOR NITROGEN GAS BOOSTER INCL. CRS	AFC	04-01-22	07-01-22	21-01-22		-6 days	0078
17811-45B	02	BU-20-VD-303-IN-DSH-0091	CALCULATION & DATA SHEET OF CONTROL VALVES / ON-OFF VALVES FOR EMERGENCY INSTRUMENT AIR COMPRESSOR INCL. CRS	AFC	04-01-22	07-01-22	21-01-22		-6 days	0078
17811-46A	01	BU-20-VD-303-IN-DIG-0044	ARCHITECTURE DIAGRAM FOR NITROGEN GAS BOOSTER	IFA	02-02-21				#VALUE!	
17811-46B	01	BU-20-VD-303-IN-DIG-0094	ARCHITECTURE DIAGRAM FOR EMERGENCY INSTRUMENT AIR COMPRESSOR	IFA	02-02-21				#VALUE!	
17811-47	00	BU-20-VD-303-IN-DSH-0045	WORKSTATION DRAWING AND DATA SHEET	IFA	30-01-21				250 days	
17811-48	00	BU-20-VD-303-PR-PRC-0047	HAZOP AND SIL STUDY PROCEDURE	IFI	02-08-21	24-09-21	08-10-21		71 days	0026
17811-49A	01	BU-20-VD-303-EL-DIG-0049	SINGLE LINE DIAGRAM FOR POWER DISTRIBUTION PANEL FOR NITROGEN GAS BOOSTER INCL. CRS	IFA	31-01-22	10-01-22	24-01-22		-7 days	0081

17811-49B	02	BU-20-VD-303-EL-DIG-0097	SINGLE LINE DIAGRAM FOR POWER DISTRIBUTION PANEL FOR EMERGENCY INSTRUMENT AIR COMPRESSOR INCL. CRS	IFA	31-01-22	10-01-22	24-01-22			-7 days	0081
17811-50A	02	BU-20-VD-303-EL-LST-0050	POWER CABLE SCHEDULE & LIST FOR NITROGEN GAS BOOSTER INCL. CRS	AFC	30-12-21	06-01-22	20-01-22			-5 days	0075
17811-50B	02	BU-20-VD-303-EL-LST-0098	POWER CABLE SCHEDULE & LIST FOR EMERGENCY INSTRUMENT AIR COMPRESSOR INCL. CRS	AFC	30-12-21	06-01-22	20-01-22			-5 days	0075
17811-52A	01	BU-20-VD-303-IN-DSH-0015	CALCULATION & DATA SHEET OF SAFETY VALVE FOR NITROGEN GAS BOOSTER INCL. CRS	IFA	18-10-21	27-10-21	10-11-21			48 days	0042
17811-52B	01	BU-20-VD-303-IN-DSH-0068	CALCULATION & DATA SHEET OF SAFETY VALVE FOR EMERGENCY INSTRUMENT AIR COMPRESSOR INCL. CRS	IFA	26-10-21	27-10-21	10-11-21			48 days	0042
17811-53A	03	BU-20-VD-303-IN-LST-0038	INSTRUMENT CABLE LIST & SCHEDULE FOR NITROGEN GAS BOOSTER INCL. CRS	AFC	04-01-22	06-01-22	20-01-22			-5 days	0075
17811-53B	02	BU-20-VD-303-IN-LST-0088	INSTRUMENT CABLE LIST & SCHEDULE FOR EMERGENCY INSTRUMENT AIR COMPRESSOR INCL. CRS	AFC	04-01-22	06-01-22	20-01-22			-5 days	0075
17811-54A	01	BU-20-VD-303-EL-DIG-0052	COMPRESSOR MOTOR CURVE FOR NITROGEN GAS BOOSTER INCL. CRS	IFA	30-08-21	06-01-22	20-01-22			-5 days	0077
17811-54B	01	BU-20-VD-303-EL-DIG-0100	COMPRESSOR MOTOR CURVE FOR EMERGENCY INSTRUMENT AIR COMPRESSOR INCL. CRS	IFA	18-01-22	06-01-22	20-01-22			-5 days	0077
17811-55	00	BU-20-VD-303-ME-LST-0056	Special tool list	IFI	15-02-22					#VALUE!	
17811-56A	02	BU-20-VD-303-IN-LST-0057	MODBUS LIST FOR NITROGEN GAS BOOSTER INCL. CRS	IFA	22-02-22					#VALUE!	
17811-56B	02	BU-20-VD-303-IN-LST-0102	MODBUS LIST FOR EMERGENCY INSTRUMENT AIR COMPRESSOR INCL. CRS	IFA	22-02-22					#VALUE!	
17811-57A	00	BU-20-VD-303-EL-DWG-0058	LV DISTRIBUTION PANEL DRAWING FOR NITROGEN GAS BOOSTER	IFA	25-07-21	21-10-21	04-11-21			52 days	0040
17811-57B	00	BU-20-VD-303-EL-DWG-0059	LV DISTRIBUTION PANEL DRAWING FOR EMERGENCY INSTRUMENT AIR COMPRESSOR	IFA	25-07-21	21-10-21	04-11-21			52 days	0040
17811-59A	01	BU-20-VD-303-ME-DWG-0024	RECIPROCATING COMPRESSOR DETAIL DRAWING WITH PARTS LIST FOR NITROGEN GAS BOOSTER	IFI	15-02-22					#VALUE!	
17811-59B	01	BU-20-VD-303-ME-DWG-0077	RECIPROCATING COMPRESSOR DETAIL DRAWING WITH PARTS LIST FOR EMERGENCY INSTRUMENT AIR COMPRESSOR	IFI	15-02-22					#VALUE!	
17811-65A	02	BU-20-VD-303-EL-LST-0048	ELECTRICAL LOAD LIST FOR NITROGEN GAS BOOSTER	AFC	26-10-21	29-10-21	12-11-21			46 days	0043
17811-65B	02	BU-20-VD-303-EL-LST-0096	ELECTRICAL LOAD LIST FOR EMERGENCY INSTRUMENT AIR COMPRESSOR	IFA	26-10-21	29-10-21	12-11-21			46 days	0043
17811-70	00	BU-20-VD-303-DC-VDR-0062	FINAL DATA BOOK FOR RECIPROCATING COMPRESSOR & NITROGEN GAS BOOSTER	IFI	after FAT					#VALUE!	
17811-71A	00	BU-20-VD-303-PI-DWG-0030	3D MODEL FOR NITROGEN GAS BOOSTER	IFA	with GAD					#VALUE!	
17811-71B	00	BU-20-VD-303-PI-DWG-0081	3D MODEL FOR EMERGENCY INSTRUMENT AIR COMPRESSOR	IFA	with GAD					#VALUE!	
17811-72A	03	BU-20-VD-303-IN-INX-0032	INSTRUMENT INDEX FOR NITROGEN GAS BOOSTER INCL. CRS	IFA	31-01-22					#VALUE!	
17811-72B	02	BU-20-VD-303-IN-INX-0083	INSTRUMENT INDEX FOR EMERGENCY INSTRUMENT AIR COMPRESSOR INCL. CRS	AFC	31-01-22					#VALUE!	
17811-73	02	BU-20-VD-303-PC-SCH-0003	TIME SCHEDULE	IFI	04-10-21	05-10-21	19-10-21			64 days	0028
17811-74	00	BU-20-VD-303-PC-MRP-0004	MONTHLY PROGRESS REPORT	IFR	monthly	14-09-21	28-09-21			79 days	0020
17811-75	02	BU-20-VD-303-PR-LST-0063	TIE-IN POINT LIST	AFC	15-11-21	12-11-21	26-11-21			36 days	0050
17811-77	03	BU-20-VD-303-PR-LST-0065	PIPING LINE LIST	AFC	15-02-22					#VALUE!	
