







OWNER:  شرکت سست و سویی توهم ایران (سایه و نقشه)	BUSHEHR PETROCHEMICAL COMPANY MEG PLANT						EPC CONTRACTOR:  Chagalesh-Enerchimi-Steam Joint Venture BUPC-MEG PLANT PROJECT		
	TIME SCHEDULE								
MC :  شرکت سست و سویی توهم ایران (سایه و نقشه)	Project	Area	Phase	Unit	Dis.	Doc.	Seq.	Contract No : 52-98/445	
Owner Document Number: 17811-73	BU	20	VD	303	PC	SCH	0003	Rev.:	Page
								01	1 of 3

- Start date shall be based on advanced payment.
 - Duration shall be based on PO
 Every step of WBS (E,P,C) shall be breakdown into 2 parts - Air compressor and Nitrogen compressor


TIME SCHEDULE

General comments:
 Time Schedule shall be prepared as follow:
 - It shall be provided based on WBS
 - WBS shall be as below with specified weight factor:
 Key Milestones 0% (Containing: Down-payment/KOM/PIM)
 Engineering 10% (Containing: any Engineering documents mandatory for the PIM)
 Procurement 45%
 Fabrication 40%
 Final Inspection & Release note 2%
 Shipment 2%
 FDB 1%
 -Procurement shall be in details based on materials & Equipment to be supplied as per Sub Vendor List.
 - documents requirement for PIM shall be separately specified under Eng.
 - Start date and finish date of project shall be indicated based on PO of the project.
 - All the Tasks & Summary Tasks shall be "Auto Schedule" not "Manually Schedule".
 -Critical Tasks & Summary Tasks shall be illustrated.

 شرکت سست و سویی توهم ایران (سایه و نقشه)	 Chagalesh-Enerchimi-Steam Joint Venture BUPC-MEG PLANT PROJECT	BUSHEHR PETROCHEMICAL COMPANY MEG PLANT
Document Review		
Issue Purpose:	IFA	
Result Code: AP,AN,CM,RE,NC	CM	
Next Status : IFC,IFA,IFI,AFC,AB	IFA	
Responsible Department	PROCUREMENT	
Commented Date	9/15/2021	
Approval or review hereunder shall not be construed to relieve Vendor / Subcontractor of his responsibilities and liability under the contract.		

	KP	PW	
	KP	PW	
	Checked	Approved	AC Code
Class: 1		Phase: P	

00	21/07/2021	For approval	JR
Rev.	Date	Purpose of Issue	Prepared

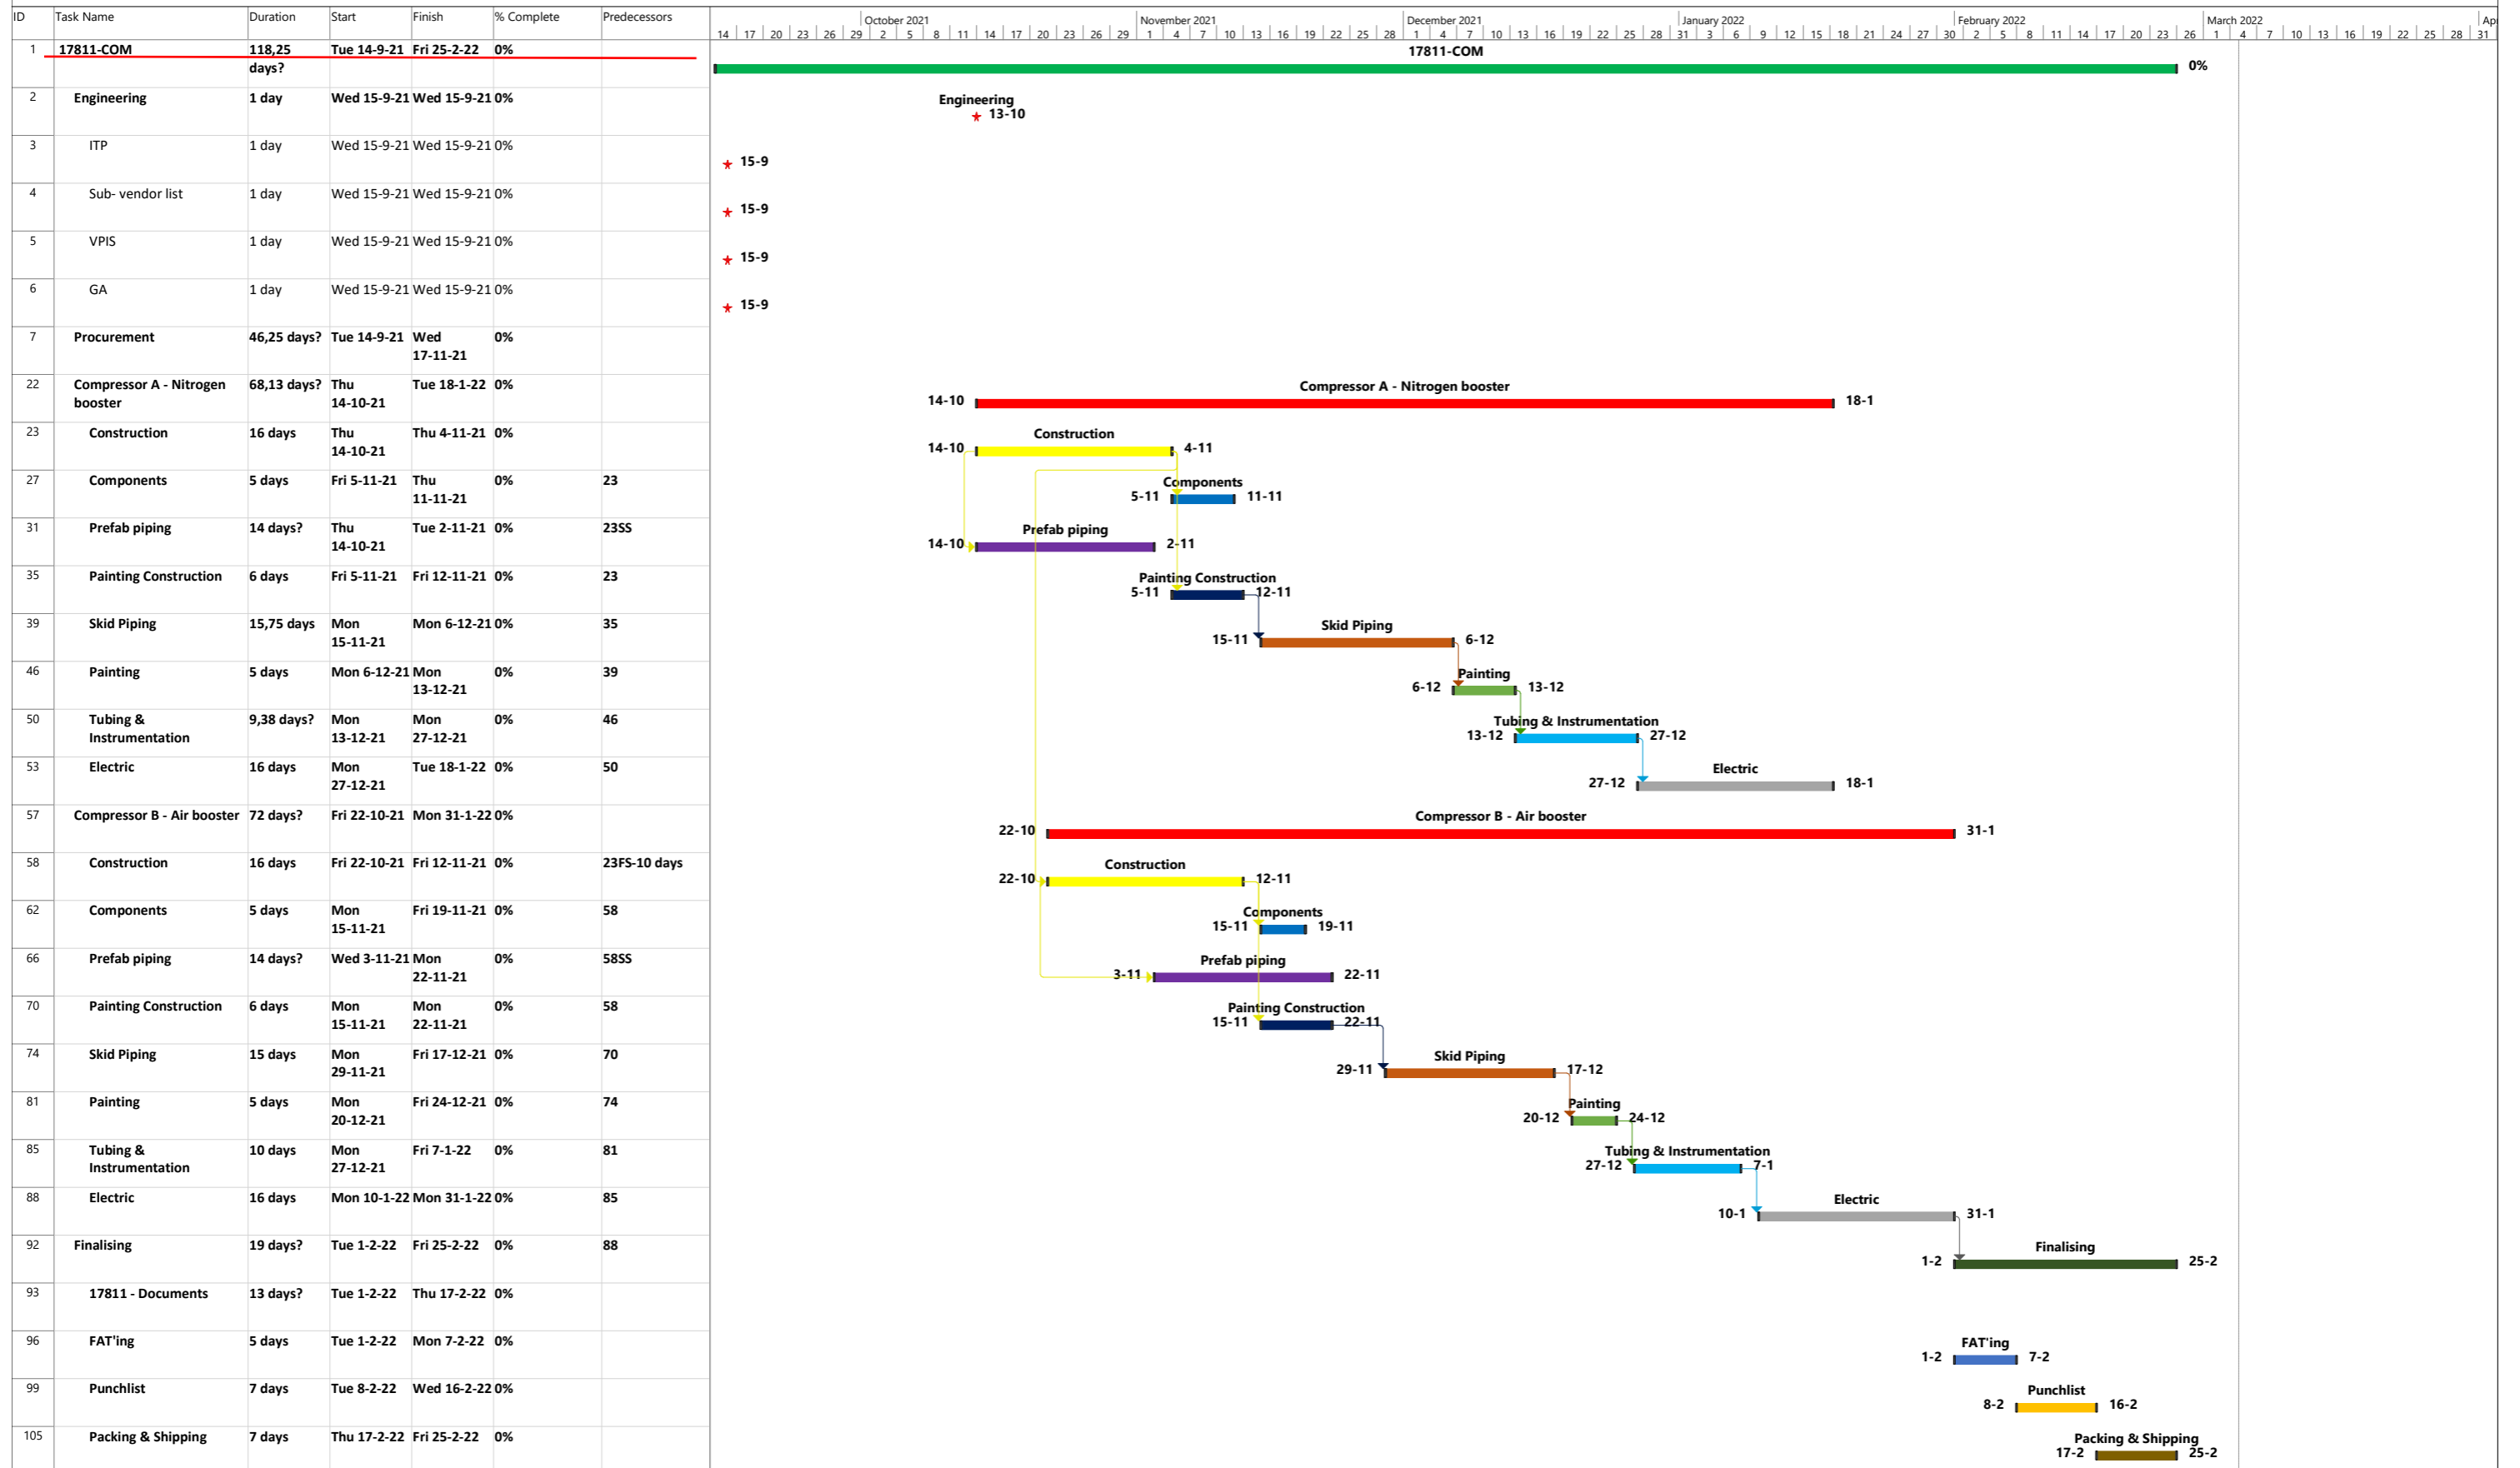

Project: Project 17811 Rev1 Date: Tue 31-8-21	Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Manual Progress
	Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	
	Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Progress	
